

Id	Modo de tarea	Texto1	Task Name	Duración	Comienzo	Fin	Gantt Chart Timeline						
							20/03	27/03	03/04	10/04	17/04	24/04	01/05
1			RECONSTRUCCION SISTEMA REDES ACUEDUCTO POSTRER RIO	260 días	sáb 09/04/22	mar 07/02/23	[Gantt bar spanning from 09/04/22 to 07/02/23]						
2		A	REDES DISTRIBUCIÓN	260 días	sáb 09/04/22	mar 07/02/23	[Gantt bar spanning from 09/04/22 to 07/02/23]						
3		1	PRELIMINARES	15 días	sáb 09/04/22	mié 27/04/22	[Gantt bar from 09/04/22 to 27/04/22]						
4		2	MOVIMIENTO DE TIERRA:	55 días	mié 27/04/22	jue 30/06/22	[Gantt bar from 27/04/22 to 30/06/22]						
5		3	SUMINISTRO DE TUBERÍAS	5 días	mar 12/04/22	lun 18/04/22	[Gantt bar from 12/04/22 to 18/04/22]						
6		4	COLOCACIÓN DE TUBERIAS	140 días	lun 18/04/22	mié 28/09/22	[Gantt bar from 18/04/22 to 28/09/22]						
7		5	SUMINISTRO Y COLOCACIÓN DE PIEZAS ESPECIALES	140 días	lun 18/04/22	mié 28/09/22	[Gantt bar from 18/04/22 to 28/09/22]						
8		6	SUMINISTRO Y COLOCACIÓN DE VÁLVULAS	140 días	lun 18/04/22	mié 28/09/22	[Gantt bar from 18/04/22 to 28/09/22]						
9		7	ACOMETIDAS EN POLIETILENO	120 días	lun 27/06/22	lun 14/11/22	[Gantt bar from 27/06/22 to 14/11/22]						
10		8	PRUEBA HIDROSTÁTICA EN TUBERÍAS	7 días	lun 14/11/22	mar 22/11/22	[Gantt bar from 14/11/22 to 22/11/22]						
11		9	DE: DEMOLICIONES	3 días	mar 22/11/22	vie 25/11/22	[Gantt bar from 22/11/22 to 25/11/22]						
12		10	REPOSICIÓN DE ACERAS Y CONTENES	8 días	vie 25/11/22	lun 05/12/22	[Gantt bar from 25/11/22 to 05/12/22]						
13		11	ASFALTO	45 días	lun 05/12/22	jue 26/01/23	[Gantt bar from 05/12/22 to 26/01/23]						



Project: Cronograma Postrer Ri
Date: vie 18/03/22

Task	[Solid bar]	Inactive Milestone	[Diamond]	Start-only	[C]	Critical Split	[Dotted bar]
Split	[Dotted bar]	Inactive Summary	[Hollow bar]	Finish-only	[J]	Progress	[Thin solid bar]
Milestone	[Diamond]	Manual Task	[Solid bar]	External Tasks	[Thin solid bar]	Manual Progress	[Thick solid bar]
Summary	[Hollow bar]	Duration-only	[Thin solid bar]	External Milestone	[Diamond]		
Project Summary	[Hollow bar]	Manual Summary Rollup	[Thin solid bar]	Deadline	[Down arrow]		
Inactive Task	[Thin solid bar]	Manual Summary	[Hollow bar]	Critical	[Thick solid bar]		


Id	Modo de tarea	Texto1	Task Name	Duración	Comienzo	Fin	Gantt Chart											
							20/03	27/03	03/04	10/04	17/04	24/04	01/05	08/05	15/05	22/05	29/05	05/06
14		12	SEÑALIZACIÓN, CONTROL, SEGURIDAD EN LA OBRA Y MANEJO DEL TRANSITO	180 días	mié 13/04/22	mié 09/11/22												
15		14	LIMPIEZA CONTINUA Y FINAL	10 días	jue 26/01/23	mar 07/02/23												
16		B	VARIOS	5 días	mar 12/04/22	lun 18/04/22												

Project: Cronograma Postrer Ri
Date: vie 18/03/22

Task		Inactive Milestone		Start-only		Critical Split	
Split		Inactive Summary		Finish-only		Progress	
Milestone		Manual Task		External Tasks		Manual Progress	
Summary		Duration-only		External Milestone			
Project Summary		Manual Summary Rollup		Deadline			
Inactive Task		Manual Summary		Critical			



julio							agosto							septiembre							octubre							noviembre							diciembre							enero							febrero						
19/06	26/06	03/07	10/07	17/07	24/07	31/07	07/08	14/08	21/08	28/08	04/09	11/09	18/09	25/09	02/10	09/10	16/10	23/10	30/10	06/11	13/11	20/11	27/11	04/12	11/12	18/12	25/12	01/01	08/01	15/01	22/01	29/01	05/02	12/02																					

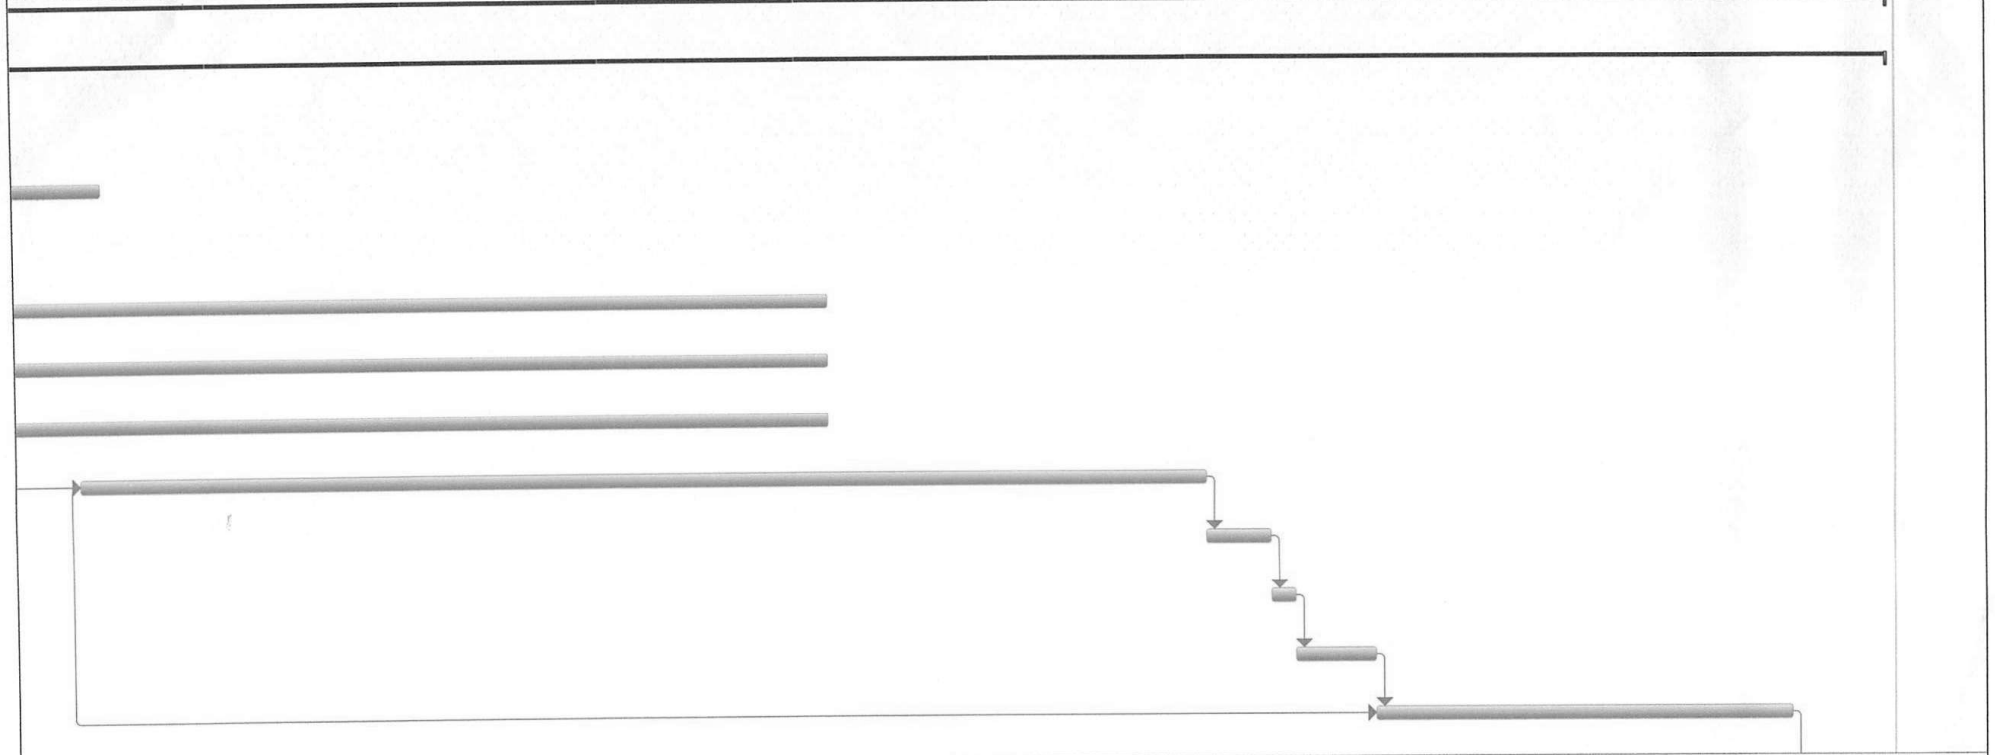


Project: Cronograma Postrer Ri
Date: vie 18/03/22

Task		Inactive Milestone		Start-only		Critical Split	
Split		Inactive Summary		Finish-only		Progress	
Milestone		Manual Task		External Tasks		Manual Progress	
Summary		Duration-only		External Milestone			
Project Summary		Manual Summary Rollup		Deadline			
Inactive Task		Manual Summary		Critical			



julio							agosto							septiembre							octubre							noviembre							diciembre							enero							febrero						
19/06	26/06	03/07	10/07	17/07	24/07	31/07	07/08	14/08	21/08	28/08	04/09	11/09	18/09	25/09	02/10	09/10	16/10	23/10	30/10	06/11	13/11	20/11	27/11	04/12	11/12	18/12	25/12	01/01	08/01	15/01	22/01	29/01	05/02	12/02																					

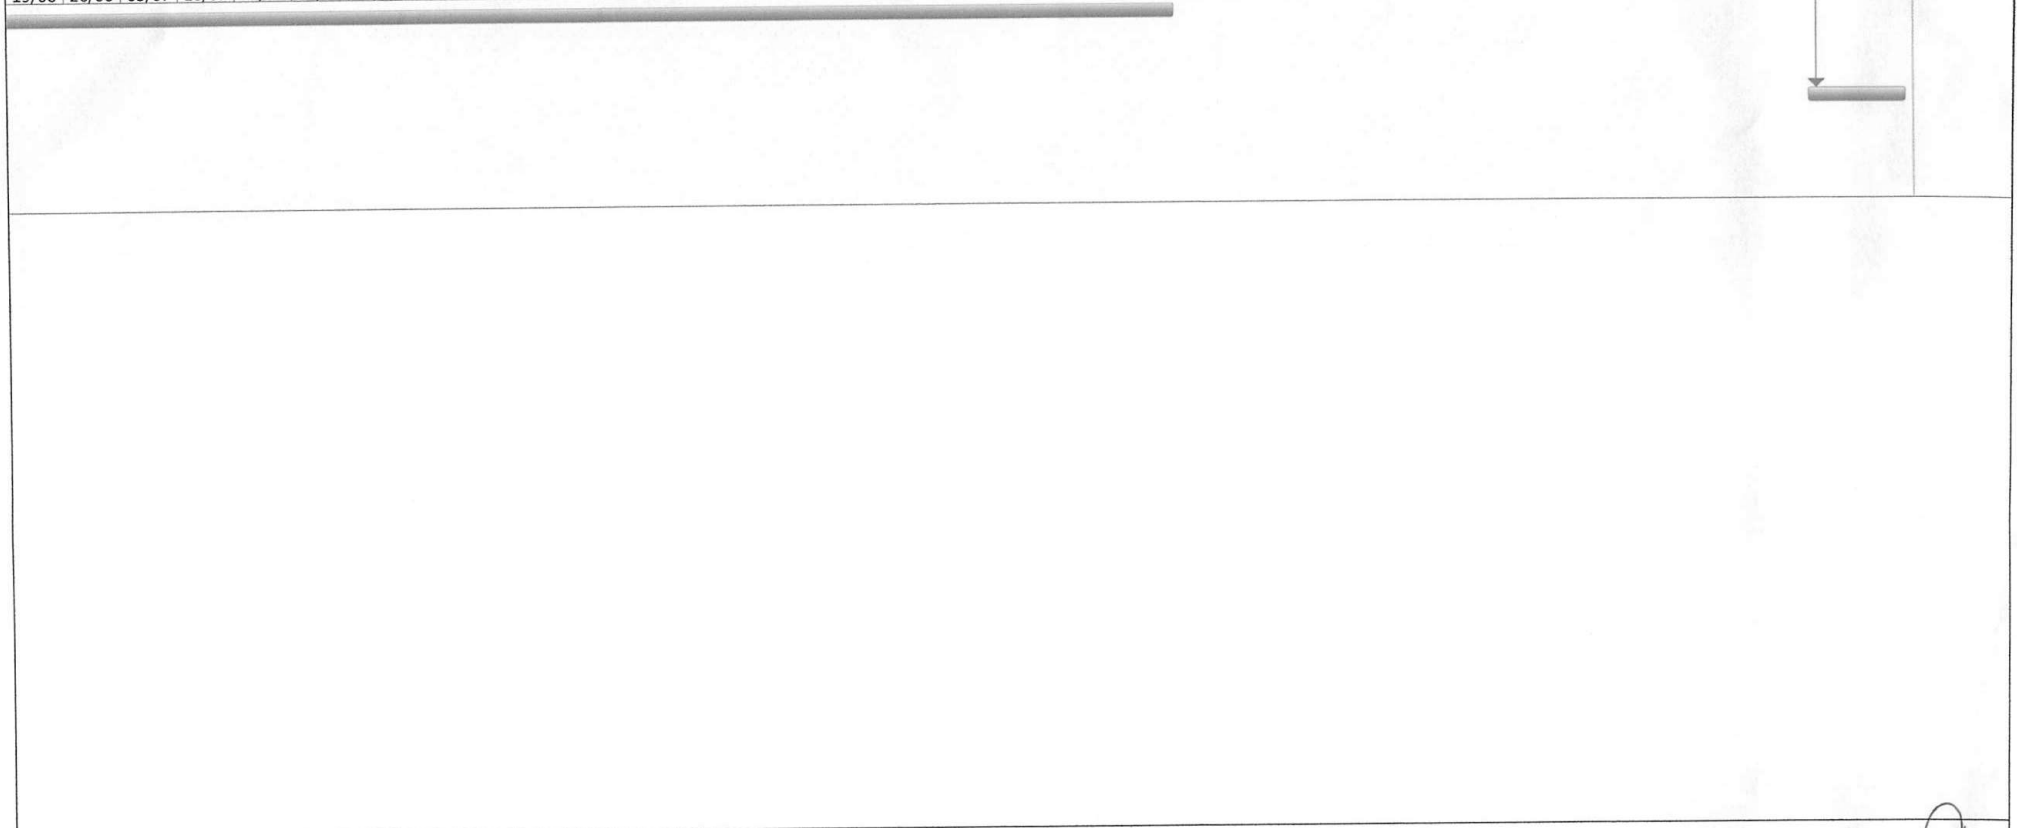

Project: Cronograma Postrer Ri
Date: vie 18/03/22

Task		Inactive Milestone		Start-only		Critical Split	
Split		Inactive Summary		Finish-only		Progress	
Milestone		Manual Task		External Tasks		Manual Progress	
Summary		Duration-only		External Milestone			
Project Summary		Manual Summary Rollup		Deadline			
Inactive Task		Manual Summary		Critical			

